wind & water works

Update: Upcoming Wind Farm Site Decisions and tender planning

Camiel van der Hout
Ministry of Economic Affairs and Climate Policy

Project highlights: Hollandse Kust (west)

Draft Wind Farm Site Decisions:

-Site Boundaries

-Nitrogen

Expected planning (to be confirmed):

-publication draft Wind Farm Site Decisions VI and VII expected: Q4 2020

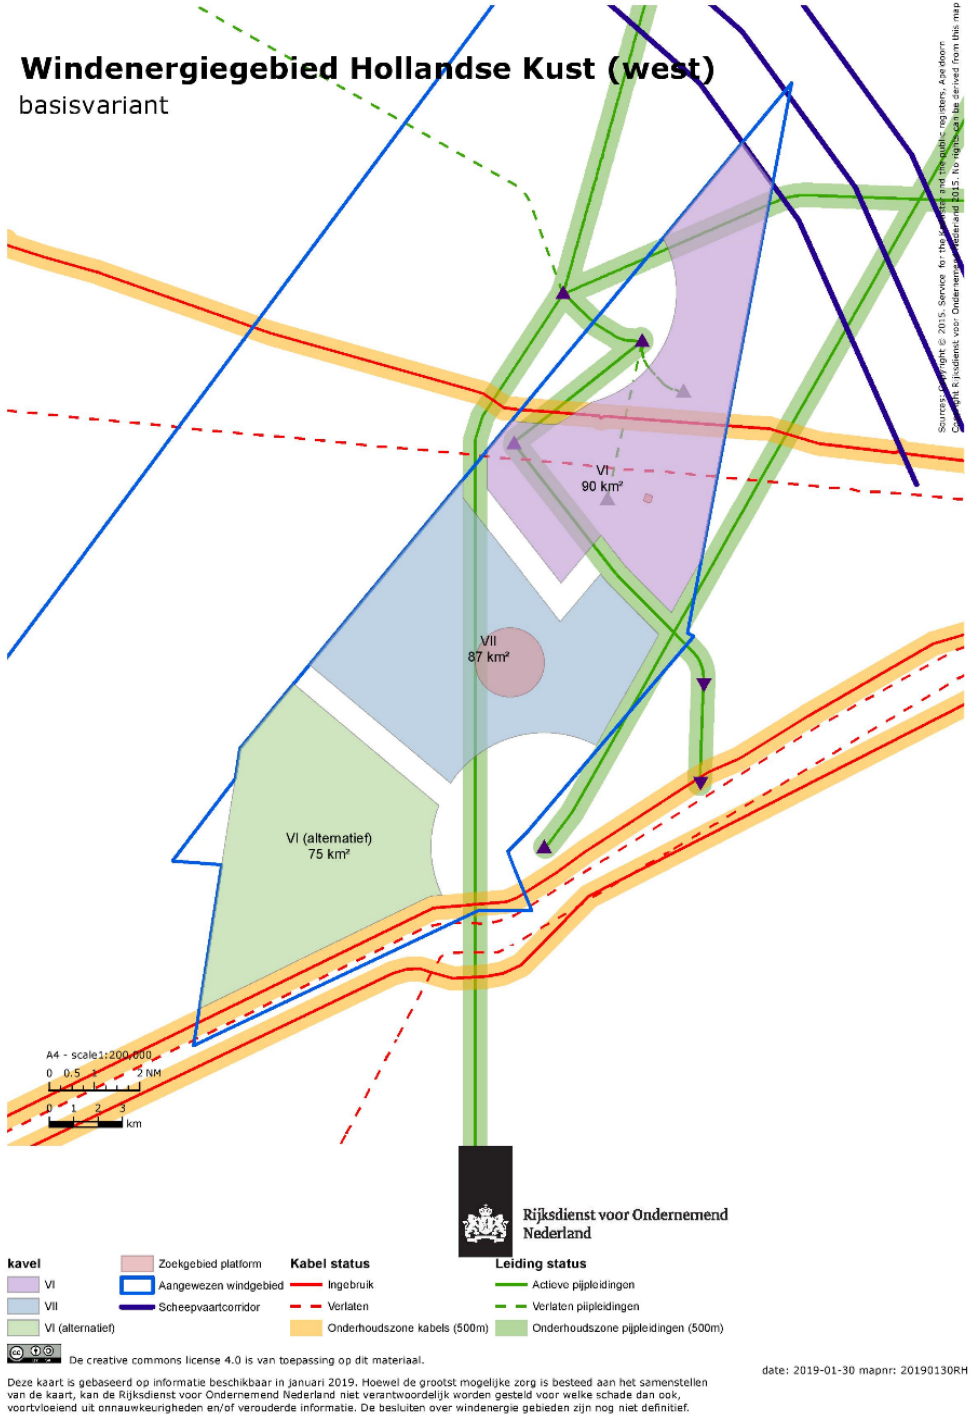

Project highlights: Hollandse Kust (west)

Tender

-2 x 0,7 GW

-consultation developers

Expected planning (to be confirmed):

-publication regulation expected: Q3 2021

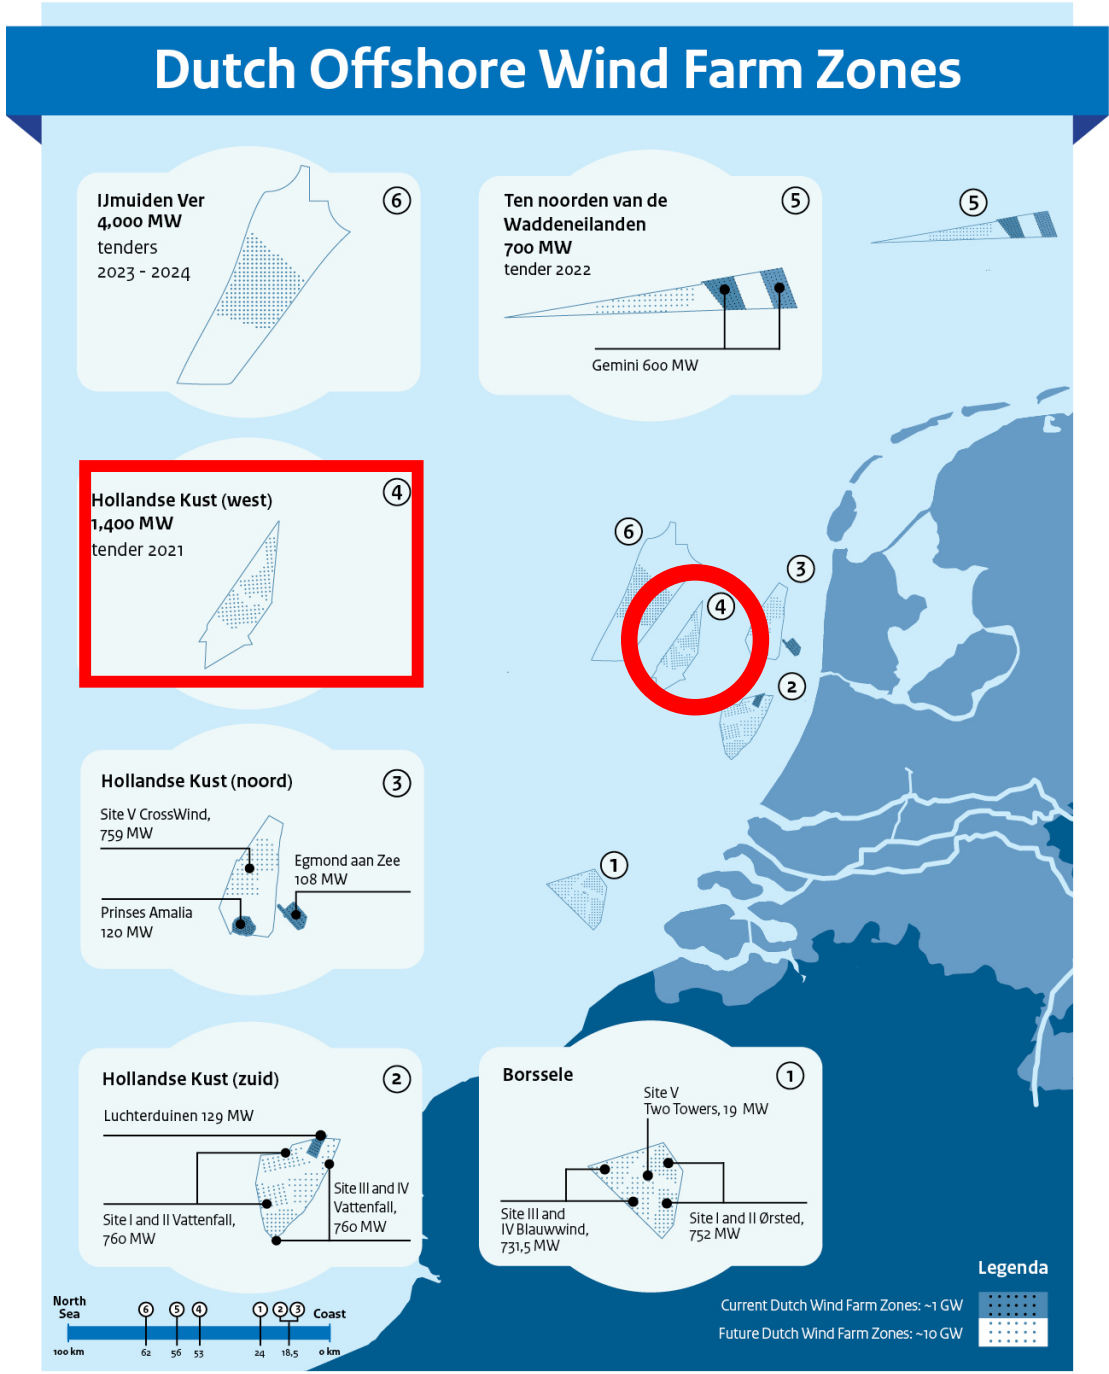

Project highlights: Hollandse Kust (west)

Detailed look at the planning

Milestone	Original planning	Expected planning (to be confirmed)
Draft wind farm site decisions	Q4 2019	Q4 2020
Definitive wind farm site decisions	Q2 2020	Q2 2021
Publication tender regulation	Tender sites Q2 2021	Q3 2021
Opening date tender		Q4 2021
Closing date tender		Q1 2022
Winner announced		Q2 2022
Commissioning HKW-alpha OHVS platform	Q1 2024	Not adjusted
Expected commissioning windfarm HKW-VI (alpha)	Expected commissioning windfarm 2025-2026	Not adjusted
Commissioning HKW-beta OHVS platform	Q1 2026	Not adjusted
Expected commissioning windfarm HKW-VII (beta)	Expected commissioning windfarm 2025-2026	Not adjusted

Project highlights: Ten noorden van de Waddeneilanden

Planning

-publication Draft Memorandum Scope and Level of Detail expected : Q4 2020

-publication draft Wind Farm Site Decision expected : Q1-Q2 2021

-tender expected : Q4 2022 (0,7 GW)

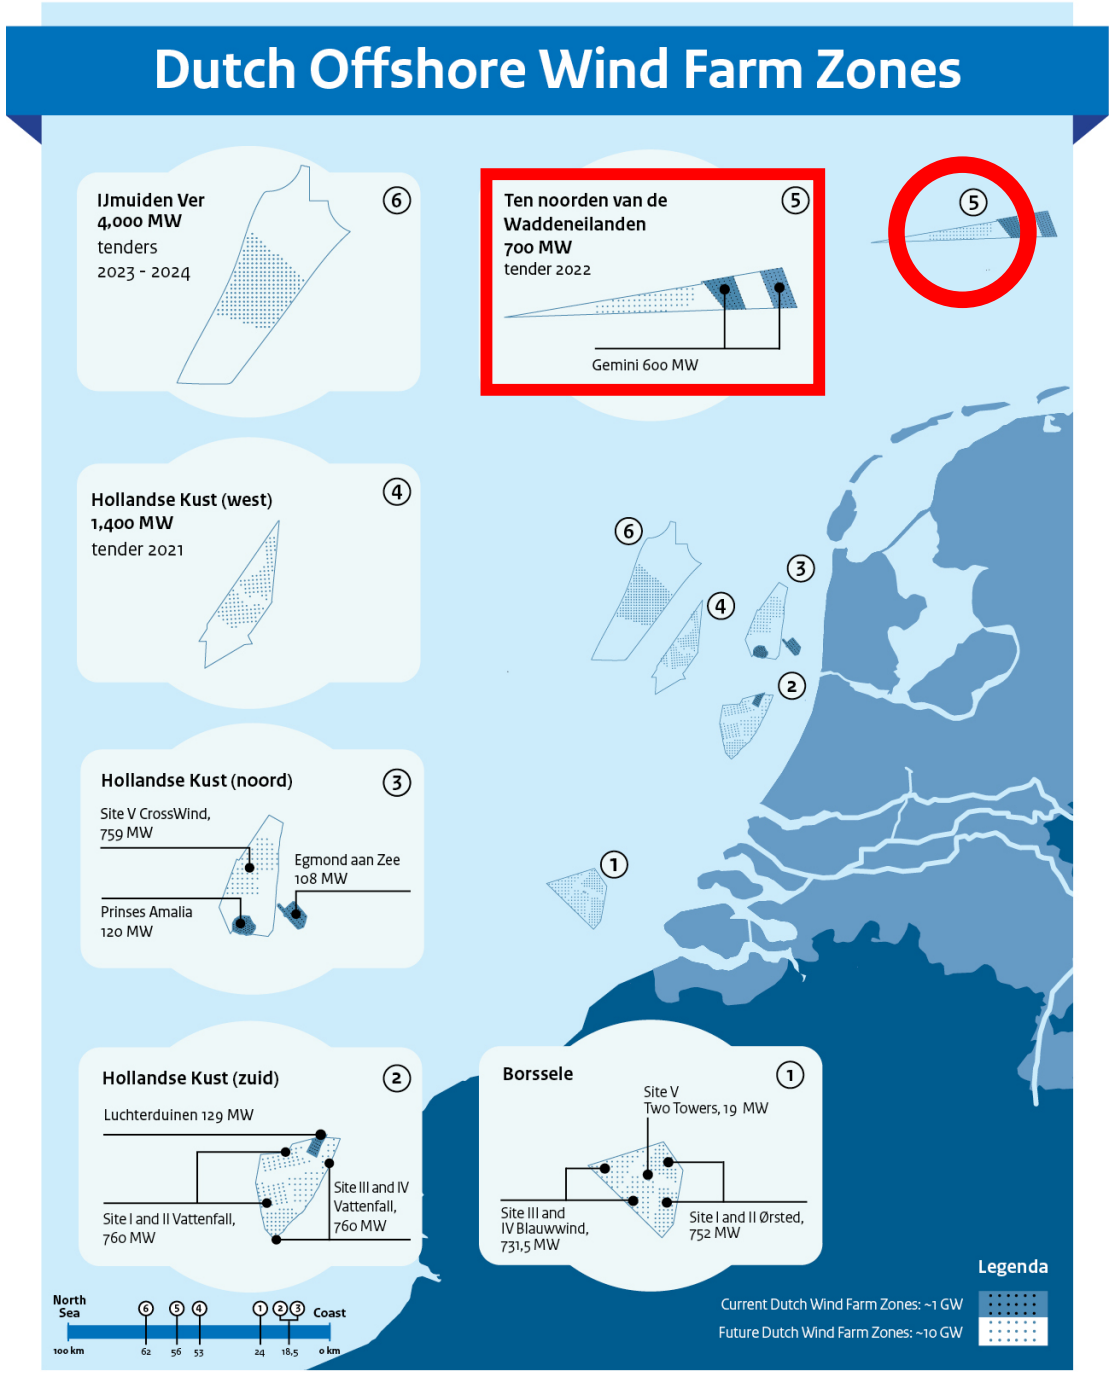

Project highlights: IJmuiden Ver

Planning

-publication draft Wind Farm Site Decisions expected: Q2 2022

-tender I & II (2 x 1 GW) expected : Q4 2023

-tender III and IV (2 x 1 GW) expected : Q4 2025

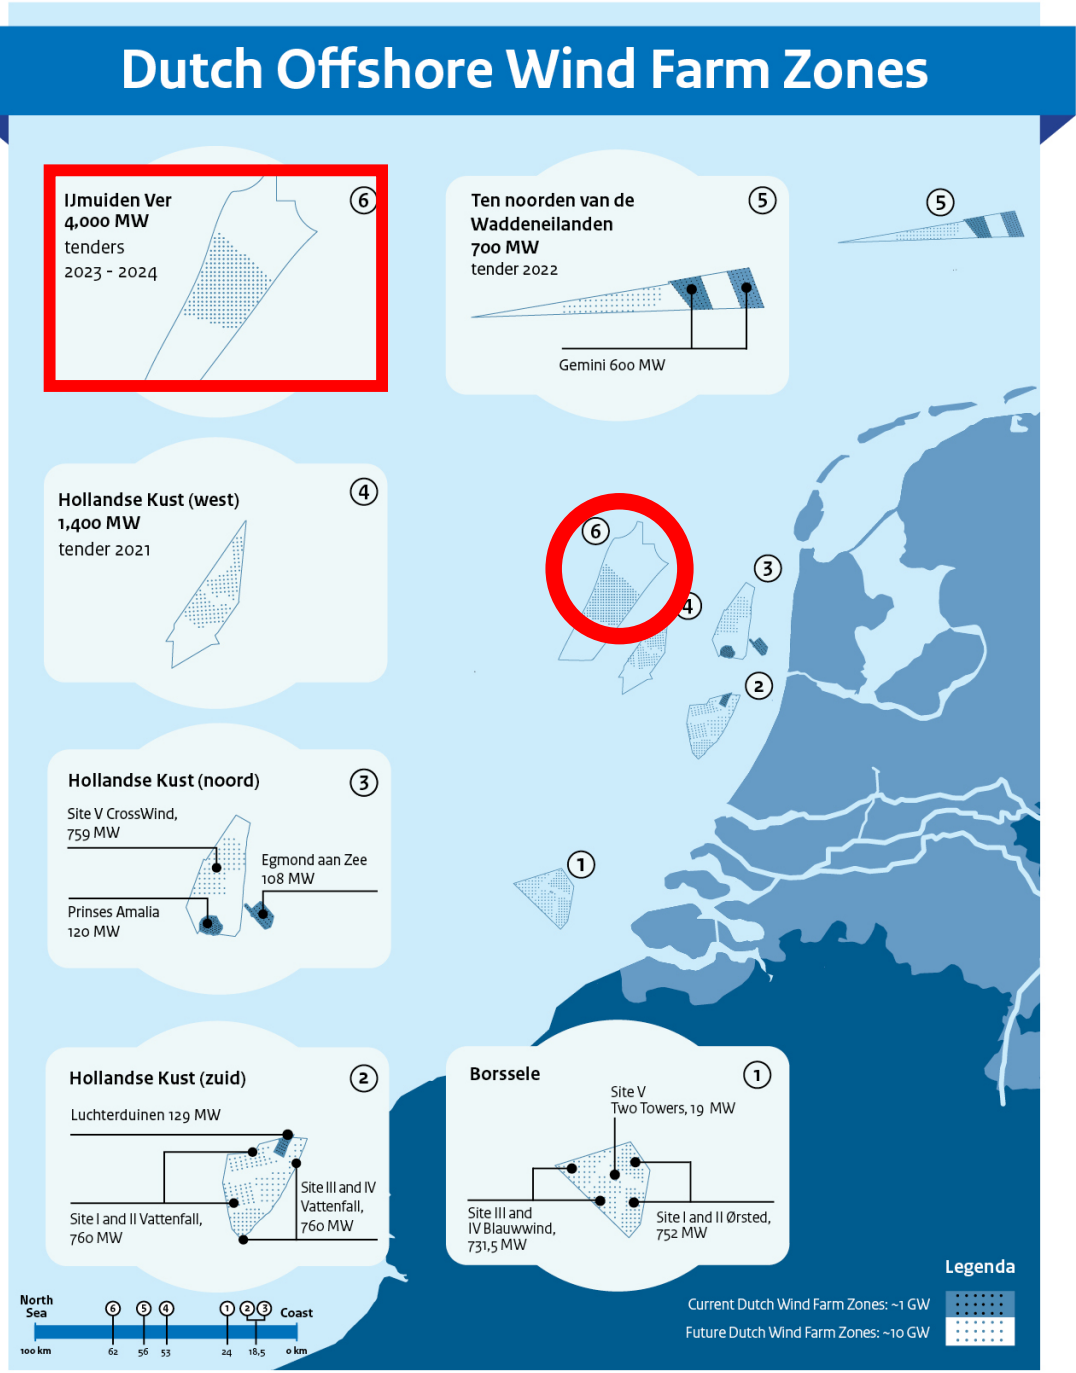

Any questions?
